Hallway + entrance panelling

Materials and nominal cuts | 25 October 2026 | All dimensions in mm unless stated

Three matching options for both rooms. The dado stays level at **1000 above the hallway floor** and **1025 above the entrance floor**. The entrance floor is 25 lower. The existing skirting is about 90 in the hallway and 75 in the entrance.

Scope	Hallway	Entrance	Combined
Dado / cap wall-face runs	11.445 m	3.930 m	15.375 m
Shaker uprights	18	7	25
Moulded frames	12	4	16
Grooved panel gross area	9.557 m2	3.439 m2	12.995 m2

Barn-door clearance changes the profile

The measured minimum gap behind the sliding door is **15 mm**. Standard caps at 18, 19 and 23 mm will not fit. E1a and E1b therefore use **9 mm deep profiles**. Shaker strips and 3 Rise frame mould are 9 mm; grooved sheets are 6 mm. The maximum 9 mm projection leaves 6 mm before adhesive or wall variation. The selected 15 mm-deep dado uses the full gap and cannot be used on E1. Dry-fit through the full door travel before fixing. Do not put the standard cap on E1.

Option	Main purchase allowance	Barn-wall detail
1. Simple Shaker	2 sheets of 9 mm MDF, 2440 x 1220; 8 standard cap lengths, 2400.	One 2400 length of 12 high x 9 deep cap; can be cut from the MDF offcut.
2. Fine moulded frames	23 Wickes 121300 (28 x 9 x 2400); 8 Wickes 121175 (29 x 15 x 2400).	E1 dado uses the same 28 x 9 mould; included in the main purchase allowance.
3. Vertical grooved sheets	7 sheets, 2440 x 1220 x 6; 8 lengths of each standard cap part, 2400.	One 2400 length of 70 high x 9 deep flat cap replaces both standard cap parts.

All quantities include full panels behind radiators and the cabinet. Door openings, door-recess linings, doors and radiators are excluded. Small wall strips receive rail/panel only. Standard linear stock includes one spare length per listed family; the short barn-wall stock has ample offcut. Grooved sheets have no extra spare sheet.

These are planning cuts. Blank sizes include trimming stock and saw loss. Use the measured wall faces for nominal lengths; corner projections, adhesive thickness, service holes and final end returns must be fitted on site. The 3D views leave small visual gaps at run ends.

Hallway wall key

Original hallway quantities and wall positions are retained.

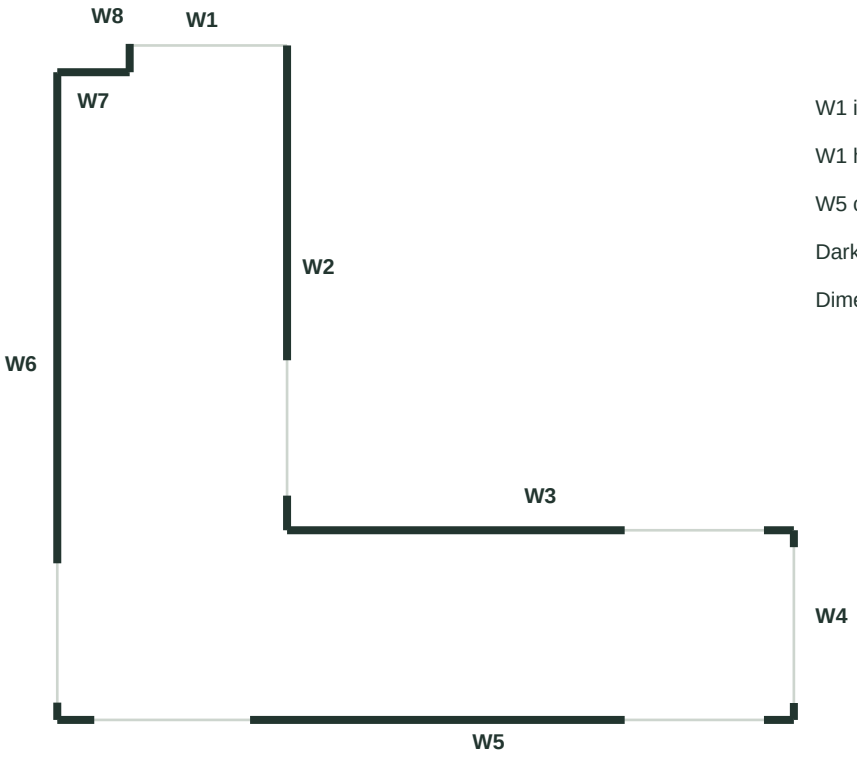

W1 is the rear door.

W1 has no rail run.

W5 connects to the entrance.

Dark lines are rail runs.

Dimensions govern; not to scale.

Run	Wall	From - to*	Rail run
W2a	Bathroom wall	0 - 2,000	2,000
W2b	Bathroom wall	2,860 - 3,080	220
W3a	Wedding-photo wall	0 - 2,145	2,145
W3b	Wedding-photo wall	3,030 - 3,220	190
W4a	Storage wall	0 - 107.5	107.5
W4b	Storage wall	1,097.5 - 1,205	107.5
W5a	Entrance and spare-bedroom wall	0 - 190	190
W5b	Entrance and spare-bedroom wall	1,075 - 3,455	2,380
W5c	Entrance and spare-bedroom wall	4,445 - 4,680	235
W6a	Kitchen and cabinet wall	0 - 110	110
W6b	Kitchen and cabinet wall	995 - 4,115	3,120
W7a	Rear boxing face	0 - 460	460
W8a	Rear recess return	0 - 180	180

*Positions run clockwise from the numbered wall start. W4 assumes the cupboard opening is centred. The hallway survey keeps a 20 x 10 mm closure residual. W6b is 3120 long; split it into two 1560 nominal pieces for either stock length.

Entrance wall key

E1 starts beside the connecting doorway and runs towards the front door.

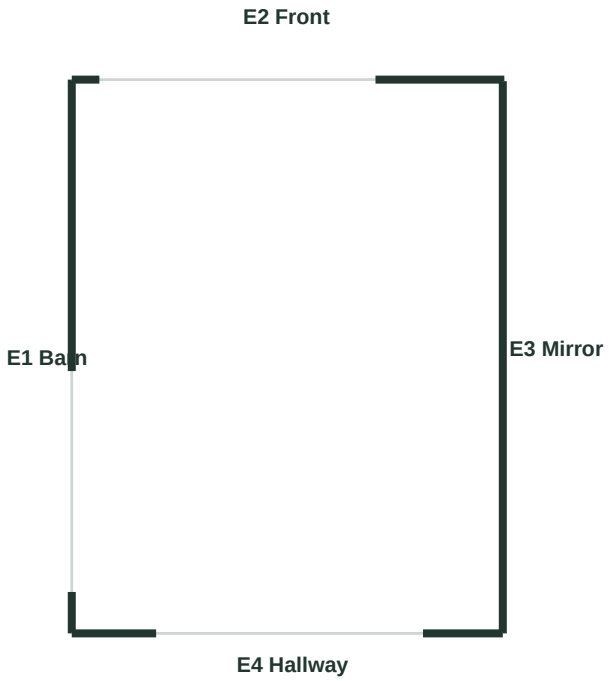

E1 uses shallow profiles.

15 mm door-to-wall gap.

E2 recess lining excluded.

E3 includes the radiator.

Dimensions govern; not to scale.

Run	Wall section	From - to	Rail run
E1a	Entrance barn wall	0 - 135	135
E1b	Entrance barn wall	855 - 1,805	950
E2a	Entrance front wall	0 - 90	90
E2b	Entrance front wall	990 - 1,410	420
E3a	Entrance mirror wall	0 - 1,800	1,800
E4a	Entrance connecting wall	0 - 260	260
E4b	Entrance connecting wall	1,130 - 1,405	275

Entrance total: 3930 mm. Of this, **1085 mm on E1** uses shallow profiles. The remaining 2845 mm uses standard profiles. Whole-room standard-profile total is 14,290 mm; add the 1085 mm shallow detail to reach 15,375 mm.

Measured wall lengths: E1 1805, E2 1410, E3 1800, E4 1405. The 5 mm width and depth differences are retained. Measure final corner cuts on site. E2 stops at the front recess edges; its 300 mm-deep returns are not panelled or included in these quantities.

The shared doorway wall is 140 mm thick excluding trim. The entrance-side frame span is 870; the hallway-side outer trim is 990. Do not extend the rail across either opening.

Option 1 / Shaker cuts

60 x 9 strips | 70 x 9 top rail | Standard cap 12 high x 18 deep; E1 cap 12 high x 9 deep

Height above local floor	Hallway	Entrance
Existing skirting top	90	75
Bottom rail lower / upper edge	95 / 155	80 / 140
Upright lower / upper edge	155 / 918	140 / 943
Upright cut length	763	803
Top rail lower / upper edge	918 / 988	943 / 1013
Cap upper edge	1000	1025

Run	Bottom rail	Uprights	Upright centres*
W2a	2,000	3 x 763	40, 940, 1,940
W3a	2,145	4 x 763	40, 600, 1,500, 2,105
W5b	2,380	4 x 763	1,111, 1,880.3, 2,649.7, 3,419
W6b	3,120	5 x 763	1,031, 1,793, 2,555, 3,317, 4,079
W7a	460	2 x 763	36, 424
E1b	950	2 x 803	891, 1,769
E2b	420	2 x 803	1,026, 1,374
E3a	1,800	3 x 803	40, 1,160, 1,760

25 uprights in total; 32.630 m of 60 mm strip. *Centres are from the whole wall start, not the run start. Bottom rails are full-span material allowances, fitted or locally interrupted around pipes.

The entrance radiator occupies E3 positions 1255-1665. The right-hand Shaker bay brackets its body and the estimated valves. Its bottom rail ends at 140 above the entrance floor, below the measured lowest bracket at 160. Confirm the pipe footprint before fixing.

All twenty rail runs are listed in the two wall-key tables. Use the standard cap on W runs and E2-E4; use the shallow cap only on E1. All other Shaker sections remain 9 mm deep.

Option 1 / strip stock

60 x 9 mm strips, 2440 long | 30 mm rough-length allowance + 3 mm saw loss; 10 mm stock-end trim

Bottom rails and uprights

Stock	Rough blank labels and lengths	Left over
1	W5b-B1: 2,410	17
2	W3a-B1: 2,175	252
3	W2a-B1: 2,030	397
4	E3a-B1: 1,830 + W7a-B1: 490	104
5	W6b-B1-1: 1,590 + E1b-U1: 833	1
6	W6b-B1-2: 1,590 + E1b-U2: 833	1
7	E1b-B1: 980 + E2b-U1: 833 + E2b-B1: 450	158
8	E2b-U2: 833 + E3a-U1: 833	758
9	E3a-U2: 833 + E3a-U3: 833	758
10	W2a-U1: 793 + W2a-U2: 793 + W2a-U3: 793	42
11	W3a-U1: 793 + W3a-U2: 793 + W3a-U3: 793	42
12	W3a-U4: 793 + W5b-U1: 793 + W5b-U2: 793	42
13	W5b-U3: 793 + W5b-U4: 793 + W6b-U1: 793	42
14	W6b-U2: 793 + W6b-U3: 793 + W6b-U4: 793	42
15	W6b-U5: 793 + W7a-U1: 793 + W7a-U2: 793	42

Use 15 strips. Supply 16, including one spare. B = bottom rail; U = upright. The long W6b bottom rail is split into -1 and -2.

MDF sheet ripping

Sheet	2440 mm strips to rip	Width used*	Width left
1	9 x 60, 8 x 70	1,151	69
2	7 x 60	441	779

*Includes 3 mm saw loss per strip. At least 20 mm remains for sheet-edge trimming. Cut the 12 x 9 shallow barn cap from the large offcut on sheet 2, or use one separate 2400 length. Confirm the supplier can cut these narrow strips.

Option 1 / rails and caps

Keep standard and shallow cap pieces labelled; they have different projections.

All 70 x 9 top rails / 2440 stock

Stock	Rough blank labels and lengths	Left over
1	W5b: 2,410	17
2	W3a: 2,175 + W3b: 220	29
3	W2a: 2,030 + E4b: 305	89
4	E3a: 1,830 + W7a: 490	104
5	W6b-1: 1,590 + E2b: 450 + E4a: 290	91
6	W6b-2: 1,590 + W5c: 265 + W2b: 250 + W5a: 220	93
7	E1b: 980 + W8a: 210 + E1a: 165 + W6a: 140 + W4a: 138 + W4b: 138 + E2a: 120	518

Standard 12 x 18 caps / 2400 stock / excludes E1

Stock	Rough blank labels and lengths	Left over
1	W5b: 2,390	2
2	W3a: 2,155 + W2b: 230	4
3	W2a: 2,010 + E4b: 285	94
4	E3a: 1,810 + W7a: 470 + E2a: 100	6
5	W6b-1: 1,570 + E2b: 430 + E4a: 270	116
6	W6b-2: 1,570 + W5c: 245 + W3b: 200 + W5a: 200 + W6a: 120	45
7	W8a: 190 + W4a: 118 + W4b: 118	1,960

E1 shallow 12 x 9 cap / one 2400 blank

Stock	Rough blank labels and lengths	Left over
1	E1b: 980 + E1a: 165	1,239

Top rails: 7 used + one spare. Standard caps: 7 used + one spare. Standard caps allow 10 extra per cut and 5 total stock-end trim. The shallow cap allows 30 extra per cut and 10 stock-end trim.

Option 2 / frame cuts

Wickes 121300: 28 wide x 9 deep | All cuts are outside long-point to outside long-point

Main dado: Wickes 121175 Pine Decorative Cover Moulding, 29 high x 15 deep x 2400. It starts at 971 above the hallway floor or 996 above the entrance floor. E1 uses Wickes 121300 Pine 3 Rise Panel Moulding, 28 high x 9 deep, starting at 997. Align the tops at 1000 / 1025; fit the 1 mm bottom-edge change at the corners. No backing strip.

Frame	Left edge*	2 horizontals	2 verticals
W2a-F1	100	820	700
W2a-F2	1,010	900	700
W3a-F1	100	460	700
W3a-F2	650	810	700
W3a-F3	1,550	500	700
W5b-F1	1,160	630	700
W5b-F2	1,950	630	700
W5b-F3	2,740	630	700
W6b-F1	1,060	810	700
W6b-F2	2,020	920	700
W6b-F3	3,090	940	700
W7a-F1	90	290	700
E1b-F1	940	780	800
E2b-F1	1,080	250	800
E3a-F1	80	1,000	800
E3a-F2	1,160	580	800

16 frames; 64 pieces; 45.100 m of mould. Both ends are mitred. Do not subtract mould widths from these outer sizes. *Left edges are from the whole numbered wall start.

Hallway: frame bottoms 190, tops 890, height 700. **Entrance:** bottoms 110, tops 910, height 800. This puts the entrance lower member at 110-138, below the measured bracket bottom at 160 and the estimated pipe entries at 150. It leaves 35 above the 75 mm skirting. Confirm pipe positions before final fitting.

Frames continue behind all three radiators. E3a-F2 is the entrance radiator frame, from 1160 to 1740. Check bracket and valve access; do not fix a member across a fitting. The 9 mm frame and dado behind the barn door leave 6 mm before adhesive within the measured gap. Frame outer sizes and positions match the rounded marking dimensions. Clear openings are 56 mm smaller than the outer height and width. Preview sections are traced from the Wickes section diagrams and scaled to published sizes. Internal radii are not dimensioned.

Option 2 / mould stock

Wickes 121300: 2400 mm stock | 30 extra per piece + 3 saw loss; 10 total end trim

Frames: H = horizontal; V = vertical. E1a-D and E1b-D = shallow dado.

Stock	Rough blank labels and lengths	Left over
1	E3a-F1H1: 1,030 + E3a-F1H2: 1,030 + W7a-F1H1: 320	1
2	E1b-D: 980 + W6b-F3H1: 970 + W7a-F1H2: 320	111
3	W6b-F3H2: 970 + W6b-F2H1: 950 + E2b-F1H1: 280 + E1a-D: 165	13
4	W6b-F2H2: 950 + W2a-F2H1: 930 + W3a-F1H1: 490	11
5	W2a-F2H2: 930 + W2a-F1H1: 850 + W3a-F3H1: 530	71
6	W2a-F1H2: 850 + W3a-F2H1: 840 + W5b-F1H1: 660	31
7	W3a-F2H2: 840 + W6b-F1H1: 840 + W5b-F1H2: 660	41
8	W6b-F1H2: 840 + E1b-F1V1: 830 + W5b-F2H1: 660	51
9	E1b-F1V2: 830 + E2b-F1V1: 830 + W5b-F2H2: 660	61
10	E2b-F1V2: 830 + E3a-F1V1: 830 + W5b-F3H1: 660	61
11	E3a-F1V2: 830 + E3a-F2V1: 830 + W5b-F3H2: 660	61
12	E3a-F2V2: 830 + E1b-F1H1: 810 + W2a-F1V1: 730	11
13	E1b-F1H2: 810 + W2a-F1V2: 730 + W2a-F2V1: 730	111
14	W2a-F2V2: 730 + W3a-F1V1: 730 + W3a-F1V2: 730	191
15	W3a-F2V1: 730 + W3a-F2V2: 730 + W3a-F3V1: 730	191
16	W3a-F3V2: 730 + W5b-F1V1: 730 + W5b-F1V2: 730	191
17	W5b-F2V1: 730 + W5b-F2V2: 730 + W5b-F3V1: 730	191
18	W5b-F3V2: 730 + W6b-F1V1: 730 + W6b-F1V2: 730	191
19	W6b-F2V1: 730 + W6b-F2V2: 730 + W6b-F3V1: 730	191
20	W6b-F3V2: 730 + W7a-F1V1: 730 + W7a-F1V2: 730	191
21	E3a-F2H1: 610 + E3a-F2H2: 610 + W3a-F3H2: 530 + W3a-F1H2: 490	138
22	E2b-F1H2: 280	2,107

22 lengths used. Supply 23, including one spare. This order includes both E1 dado runs. Cut final mitres from these blanks after a full frame dry-fit.

Shared standard rail schedule

Option 2 Wickes 121175 main dado, or EACH Option 3 standard cap component

2400 stock / standard profiles / excludes E1

Stock	Rough blank labels and lengths	Left over
1	W3a: 2,175 + W6a: 140	69
2	W2a: 2,030 + E4b: 305	49
3	E3a: 1,830 + W7a: 490	64
4	W6b-1: 1,590 + E2b: 450 + E4a: 290	51
5	W6b-2: 1,590 + W5c: 265 + W2b: 250 + W3b: 220	53
6	W5b-1: 1,220 + W5a: 220 + W8a: 210 + W4a: 138 + W4b: 138 + E2a: 120	326
7	W5b-2: 1,220	1,167

7 lengths used + one spare = 8 supplied per profile. Option 2 uses this schedule once. Option 3 uses it twice for its two standard cap parts, or once if a suitable combined cap is selected.

Option 3 ONLY: E1 shallow flat profile / separate 2400 stock

Stock	Rough blank labels and lengths	Left over
1	E1b: 980 + E1a: 165	1,239

Option 2: both E1 dado runs are already in the Wickes 121300 schedule on page 8; do not buy another shallow length. Option 3: use one 70 high x 9 deep flat cap length. Do not put the 15 mm-deep cover moulding, a projecting cap or packing behind the barn door.

Corner details

For 2400 stock, split W5b (2380) into two 1190 nominal pieces to retain 30 extra per blank. W6b remains two 1560 pieces. Allow 3 saw loss per cut and 10 total stock-end trim.

Run lengths are wall-face dimensions. Outside corners may need extra length equal to the profile projection; inside corners may need a scribed joint. Establish each end with a physical sample and the actual angle. The stock schedules include trimming allowance, but do not define final corner mitres.

Option 3 / panel cuts

6 mm grooved MDF | Widths below are nominal rectangular blanks before fitting and service cutouts

Hallway panels: **835 high**, from 95 to 930 above floor. Entrance panels: **875 high**, from 80 to 955. Standard flat cap is 55 high x 14 deep; upper lip is 15 high x 23 deep. E1 replaces both with one 70 high x 9 deep flat cap.

Run	Panel widths in wall order	Each height
W2a	1,000 + 1,000	835
W2b	220	835
W3a	1,100 + 1,045	835
W3b	190	835
W4a	107.5	835
W4b	107.5	835
W5a	190	835
W5b	1,200 + 1,180	835
W5c	235	835
W6a	110	835
W6b	1,100 + 1,100 + 920	835
W7a	460	835
W8a	180	835
E1a	135	875
E1b	950	875
E2a	90	875
E2b	420	875
E3a	1,000 + 800	875
E4a	260	875
E4b	275	875

26 panel blanks; 12.995 m2 gross. A plus sign marks a sheet joint, not a groove. Door reveals and recess returns are excluded. No area is deducted for services.

Order grooves parallel to the 2440 mm direction. Keep every panel upright; do not rotate offcuts by 90 degrees. Align joins with the factory groove pattern where possible. The render uses approximate 100 mm groove spacing and visual service holes; these holes are not cutting dimensions.

Option 3 / sheets 1-4

2440 x 1220 sheets | Cut rough row heights first, then widths; keep groove direction vertical

Sheet 1 / height offcut 744

Row	Rough height	Rough width cuts	Width left
1	840	W5b-P1: 1,205	7
2	840	W5b-P2: 1,185	27

Sheet 2 / height offcut 704

Row	Rough height	Rough width cuts	Width left
3	880	W3a-P1: 1,105 + E2a-P1: 95	9
4	840	W6b-P1: 1,105	107

Sheet 3 / height offcut 704

Row	Rough height	Rough width cuts	Width left
5	840	W6b-P2: 1,105	107
6	880	W3a-P2: 1,050 + E1a-P1: 140	19

Sheet 4 / height offcut 744

Row	Rough height	Rough width cuts	Width left
7	840	W2a-P1: 1,005 + W3b-P1: 195	9
8	840	W2a-P2: 1,005 + W5a-P1: 195	9

Each rough width includes 5 extra, plus 3 saw loss per cut and 5 row-edge trim. Rough row height is 840 for hallway-only rows, or 880 if any entrance panel shares the row. Finish each labelled panel to its own 835 or 875 height. Each sheet allows 10 total end trim and 3 per row crosscut.

Confirm usable sheet dimensions, edge quality and groove datum before purchase. A 1200 finished panel needs more than 1200 usable width once trimming is included. Re-plan that join if the supplied sheet is narrower than 1220. Keep the large height offcuts for fitting trials; they are too short for full-height panels.

Option 3 / sheets 5-7

2440 x 1220 sheets | Cut rough row heights first, then widths; keep groove direction vertical

Sheet 5 / height offcut 664

Row	Rough height	Rough width cuts	Width left
9	880	E3a-P1: 1,005 + W8a-P1: 185	19
10	880	E1b-P1: 955 + W5c-P1: 240	14

Sheet 6 / height offcut 664

Row	Rough height	Rough width cuts	Width left
11	880	W6b-P3: 925 + E4b-P1: 280	4
12	880	E3a-P2: 805 + E4a-P1: 265 + W6a-P1: 115	21

Sheet 7 / height offcut 704

Row	Rough height	Rough width cuts	Width left
13	880	W7a-P1: 465 + E2b-P1: 425 + W2b-P1: 225	91
14	840	W4a-P1: 113 + W4b-P1: 113	983

Each rough width includes 5 extra, plus 3 saw loss per cut and 5 row-edge trim. Rough row height is 840 for hallway-only rows, or 880 if any entrance panel shares the row. Finish each labelled panel to its own 835 or 875 height. Each sheet allows 10 total end trim and 3 per row crosscut.

Confirm usable sheet dimensions, edge quality and groove datum before purchase. A 1200 finished panel needs more than 1200 usable width once trimming is included. Re-plan that join if the supplied sheet is narrower than 1220. Keep the large height offcuts for fitting trials; they are too short for full-height panels.

Fitting checks and supplies

Set out both rooms from one common level before cutting final lengths.

Location	Required check
Barn door / E1	Dry-fit the 9 mm rail and frame mould with the intended adhesive. Slide the door fully both ways. Total finished projection must remain below the measured 15 mm gap.
Entrance radiator / E3	Body is 410 wide x 635 high, bottom 200; right edge 135 from the hallway corner. Lowest bracket is 160. Confirm pipes, valve reach, bracket holes and removable access.
Mirror and switches	Mirror bottom is 1190 above entrance floor; switches start at 1185. Dado top is 1025, leaving 165 and 160 respectively.
Hallway radiators	Body width 795, height about 595. Floor gaps, pipes, valve extents and bracket footprints still need measurement.
Skirting and corners	Confirm the 5 mm gap above the actual skirting top and its projection. The hallway and entrance have separate small survey closure differences.
Sockets and service holes	Template on site. Do not cut openings from estimated render positions. Keep faceplates, valves and wall-box access clear.

Consumable planning allowances

Supply	Shaker	Frames	Grooved
Adhesive, 290-310 ml cartridges	8-11	7-9	14-17
Decorators caulk	3-4	3-4	4
Fine filler	One small tub	One small tub	One small tub
Primer	About 1.5 litres	About 1.5 litres	About 3 litres
Coloured topcoat, two coats	About 4.1 litres	About 4.1 litres	About 4.1 litres

These are estimates, not coverage guarantees. Paint allowance uses about 17 m2 including lower walls and trim, two coats at 10 m2/litre, plus 20%. Confirm the selected finish and substrate preparation. Doors and radiators are excluded.

Sources and revision

Room dimensions: local survey.json, hallway plan-geometry.json and entrance-geometry.json; user corrections and reference photos through 9 October 2026. Hallway layouts preserve the prior take-off (18 uprights, 12 frames, 11.445 m rail). Entrance clearance is the measured 15 mm minimum through full sliding travel. Fine-frame sizes and positions match the rounded wall-marking PDF agreed on 25 October 2026. Material sections, layout positions and stock allowances are design proposals. Selected Option 2 products: Wickes 121175 and 121300, nominal sections verified on 20 October 2026. No supplier prices or availability are asserted.

Sequence: mark the common top line; dry-fit the barn-wall profile and radiator details; label and rough-cut stock; fit corners and service openings; fix, fill, prime and paint. Use the selected material and adhesive instructions.
